SRI BAALAMURUGAN BOREWELLS

4, gangamma Compound, Opp. Canara Bank Bus Stop, Bellary Main Road, Hebbal Bangalore - 24
Mob : 9845020536, 9901920004

WORK REPORT

			No.	
			Date :	29-04-15
Agrahara layout 8th cross				
S.No.	Particulars	Rft :	Water Yield	Remarks
1.	Size of The Borewell	165 mm		
2.	Total Deapth of The Borewell	980'		
3.	MS Casing Erected	170'		
4.	1st Water Source at the Deapth	305'		
5.	2nd Water Source at the Deapth	510'		
6.	3rd Water Source at the Deapth	780'		
7.	4th Water Source at the Deapth	930'		
8.	If any Silt, Boulders at the Deapth	—		
9.	Nature of Water	Sweet water		
10.	Moter Pump to be Used	15 HP 25 Stage		
11.	Any other Remarks	—		
12.	Total Yield of the Borewell	2'-0"		

Thanking You

Yours faithfully
For Sri Baalamurugan Borewells

GROUND WATER SURVEY REPORT

~~OPEN WELL~~/ BOREWELL
DATA OF SURVEY

a) Name of the Party : AEE. Bayarayanapura,

b) Location of the Site : Ward No. 05 B.B.M.P.

c) Area of the land : Agrahara lay out, 8.M cor

INVESTIGATION REPORT

1) GEOLOGY OF THE AREA :

2) Recommended Site for drilling :

3) Total depth to be drilled : 800'0" TO 1260'0"

4) Approx. casing pipe required : 90'0" To 198'0"

5) No. of water bearing Zones : — 1 —

6) No. of favourable spots marked : — 1 —

7) Qty. of water expected : 2" to 2½"

8) Method of survey carried out : Geo

9) Remarks :

HYDROGEOLOGIST
(M.G. RAJASHEKHAR, M.Sc., DEG., F.G.S.)

P.T.O. : Terms & Conditions

BOREWELL SITE PLAN

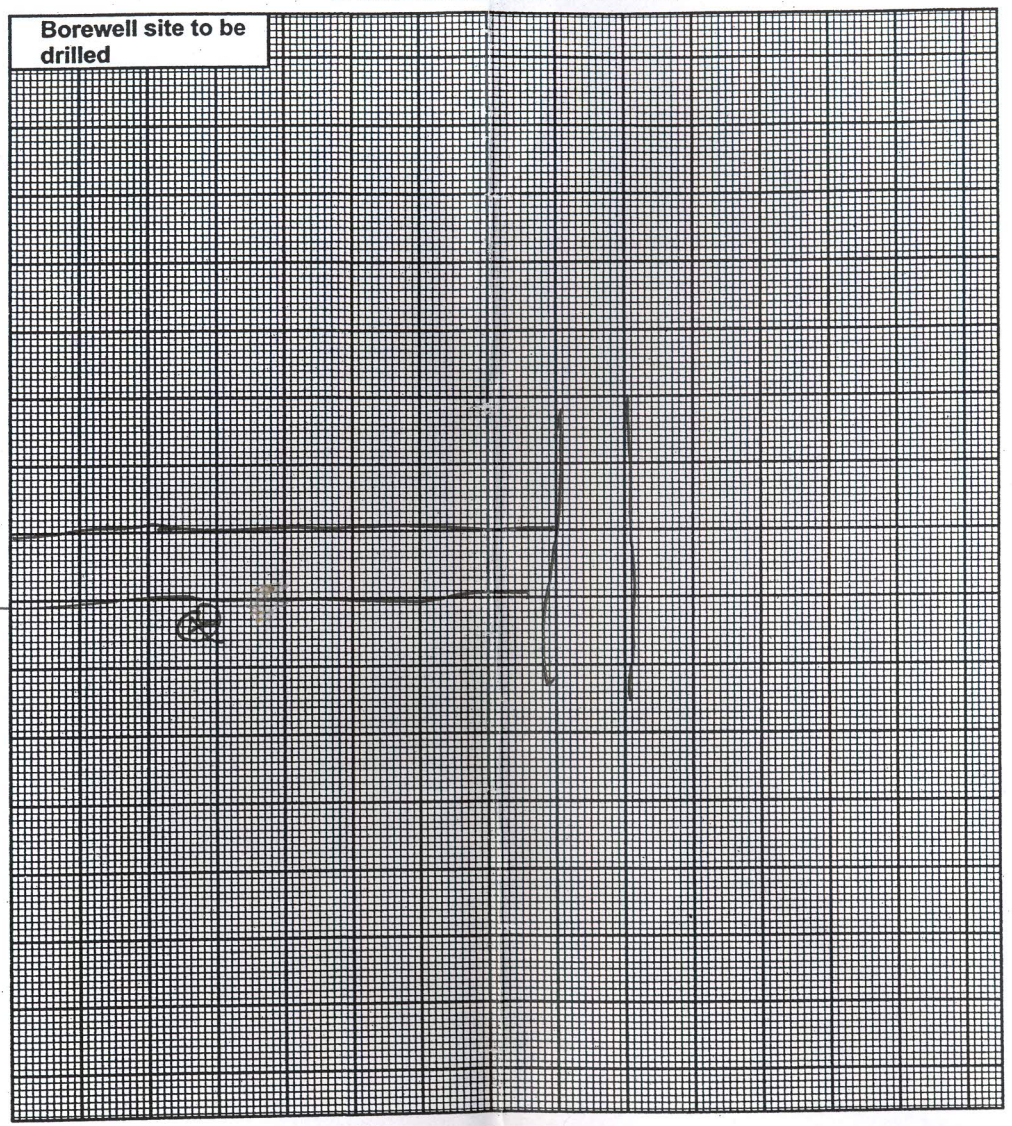

Bengaluru C8 Sub-Division

Receipt Number 807449461673
Reciept Date 28-04-2015 14:28:17
Cash Counter BESCOM - C8 SDO Cash Counter
Payor Account ID 8074494188
Person Name AEE B B M P
[redacted]
Total Payment Rs7,560.00
Mode of pay Cash
Purpose Deposits
Non Revenue category ZMMD-FEE

Seven Thousand Five Hundred Sixty Rupees Only

---------- THANK YOU ----------

BANGALORE ELECTRICITY SUPPLY COMPANY LTD

TAX INVOICE

Landis+Gyr Limited

ಲ್ಯಾಂಡಿಸ್+ಗೇರ್ ಲಿಮಿಟೆಡ್

Landis+Gyr

R. O.
No. 503, 3rd Main,
50 Feet Road, Srinagar,
Bangalore - 560 050

Branch Office
O/o Asst. Executive Engineer, (Ele)
Lingarajapura O & M Unit, BESCOM
E5 Sub-Division, HBR Layout, 3rd Block,
80 Ft. Road, Opp. BDA Complex, Bangalore.

Name AEE BBMP.

Address 8th Cross. Agrahara L/o

B.lore.

BILL No. **AE** 60462

DATE : 29/04/15 · TIME : AM/PM

TIN : 29330352183
CST No. 01153900 Dt. 10-03-2003

Sl. No.	Description	Quantity	Rate per Pc Rs.	Value Amount Rs.	P.
	Single Phase Static Energy Meter Type ~~ZCE~~, 5-30 ~~Amps~~ 3Ph		2134-84		
	Sl. Nos. C0156536.	0-1		2134-84	
	VAT @ 14.5 %			309.55	
	GRAND TOTAL			2444 39	

Name of Company **BESCOM** DVN. C-8

W.O. No. T-2357 Date 28/04/15

E.&O.E.

For **Landis+Gyr Limited.**

AE-01

ಸಹಾಯಕ ಕಾರ್ಯನಿರ್ವಾಹಕ ಇಂಜಿನಿಯರ್ (ನಿ.)

Bangalore ವಿದ್ಯುತ್ ಸರಬರಾಜು ಕಂಪನಿ ನಿಯಮಿತ

ಕ್ರ.ಸಂ.ಸ.ಕಾ.ನಿ.ಎಂ.(ವಿ) :: ಸ.ಎಂ.(ತಾಂ) : 02

(ಅಂಚೆಯ ಮೂಲಕ ಮಾತ್ರವೇ ಕಳುಹಿಸತಕ್ಕದ್ದು)

ಸಹಾಯಕ ಕಾರ್ಯನಿರ್ವಾಹಕ ಇಂಜಿನಿಯರ್ (ವಿ.)ರವರ ಕಛೇರಿ

C8 ಉಪವಿಭಾಗ,

ವಿದ್ಯುತ್ ಸರಬರಾಜು ಕಂಪನಿ ನಿಯಮಿತ

Hebbal North DIV

ದಿನಾಂಕ 25-04-2015

ಗೆ,

AEE BBMP
#8th Cross
Agrahaharalayout

-New-

ಮಾನ್ಯರೇ,

ನಿಮ್ಮ ಸ್ಥಾವರಕ್ಕೆ ವಿದ್ಯುತ್ ಮಂಜೂರಾತಿ

ಈ ಪತ್ರಕ್ಕೆ ನಮ್ಮ ಕಚೇರಿಯ 25-04-2015 ದಿನಾಂಕದ WS-02 ಸಂಖ್ಯೆಯ ಪತ್ರದ ಉಲ್ಲೇಖವಿದೆ. ಈ ಮೂಲಕ ತಮಗೆ ತಿಳಿಯಪಡಿಸುವುದೇನೆಂದರೆ, ಕೆಳಕಂಡ ನಿಬಂಧನೆಗಳ ಪ್ರಕಾರ ನಿಮಗೆ LT-6 ಅ.ಶ. 12 HP ಕಿ.ವಾ. ಗಳಿಗೆ ಮಾತ್ರ ವಿದ್ಯುತ್ ಮಂಜೂರಾತಿ/ಹೆಚ್ಚುವರಿ ವಿದ್ಯುತ್ ಮಂಜೂರಾತಿ ನೀಡಿದೆ.

1. ವಿದ್ಯುತ್‌ನ್ನು ಒಂದು ಫೇಸ್, 230ವೋಲ್ಟ್ : ಮೂರು ಫೇಸ್, 400 ವೋಲ್ಟ್‌ಗಳಲ್ಲಿ ಸರಬರಾಜು ಮಾಡಲಾಗುತ್ತದೆ.
2. ಹಾಲಿ ತಮ್ಮ ಸ್ಥಾವರಕ್ಕೆ ಅನ್ವಯಿಸುವ ವಿದ್ಯುತ್ ಜಕಾತಿಯು LT-6 ಆಗಿರುತ್ತದೆ.
3. ನೀವು ..... ಆರ್.ಕೆ.ವಿ.ಎ. ಸಾಮರ್ಥ್ಯದ ಎಲ್.ಟಿ. ಕೆಪಾಸಿಟರ್‌ನ್ನು ಅಳವಡಿಸಬೇಕು.
4. ನೀವು ..... ಅಂಪೇರ್ ಸಾಮರ್ಥ್ಯದ ವಿದ್ಯುತ್ ಪ್ರವಾಹದ ಮಿತಕ (ಲಿಮಿಟರ್)ನ್ನು ಅಳವಡಿಸುವುದು.
5. ನೀವು ..... ಅಂಪೇರ್ ಸಾಮರ್ಥ್ಯದ ಅರ್ತ್ ಲೀಕೇಜ್ ಸರ್ಕ್ಯೂಟ್ ಬ್ರೇಕರನ್ನು ಹಾಕಿಸತಕ್ಕದ್ದು. (30ma (ಮಿಲಿ ಅಂಪಿಯರ್) ಸೋರುವಿಕೆ ಪತ್ತೆ ಮಾಡುವ)
6. ನಿಮಗೆ ಸೂಚಿಸಿರುವ ಮಾರ್ಗದಲ್ಲಿ 16/4 ಗಾತ್ರದ ಭೂಗತ ಕೇಬಲ್: ಓವರ್ ಹೆಡ್ ಸೇವಾ ಸಂಪರ್ಕವನ್ನು ಹಾಕಿಸತಕ್ಕದ್ದು.
7. ಈ ಕೆಳಕಂಡ ಶುಲ್ಕ: ಠೇವಣಿಯನ್ನು ಪಾವತಿಸತಕ್ಕದ್ದು:
   (ಅ) ~~ಮೂರು~~ 2 ತಿಂಗಳ ಕನಿಷ್ಠ ಠೇವಣಿ ರೂ. 8074494188-7440 7560
   (ಆ) ಮಾಪಕ ಭದ್ರತಾ ಠೇವಣಿ ರೂ. .....
   (ಇ) ಅಂದಾಜು ವೆಚ್ಚ ರೂ. .....
   (ಈ) ಮೇಲ್ವಿಚಾರಣಾ ಶುಲ್ಕ ರೂ. .....
8. ನೀವು ಅನುಮತಿ ಪಡೆದ ವಿದ್ಯುತ್ ಗುತ್ತಿಗೆದಾರರಿಂದ ಪಡೆದ ಕಾರ್ಯಸಮಾಪನ ಮತ್ತು ಪರೀಕ್ಷಾ ವರದಿಯ ಜೊತೆಗೆ ದ್ವಿಪ್ರತಿಯಲ್ಲಿ ವೈರಿಂಗ್ ನಕ್ಷೆಯನ್ನು ಹಾಜರುಪಡಿಸತಕ್ಕದ್ದು. ಜೊತೆಗೆ ನೀವು ವಿದ್ಯುತ್ ಗುತ್ತಿಗೆದಾರರ ಚಾಲ್ತಿಯಲ್ಲಿರುವ ಅನುಮತಿ ಪ್ರತಿಯನ್ನೂ ಹಾಜರುಪಡಿಸತಕ್ಕದ್ದು.
9. ನೀವು ರಸ್ತೆ ಅಗೆಯುವ ಅಪ್ಪಣೆ ಪತ್ರವನ್ನು B.B.M.P ರವರಿಂದ ಪಡೆದು ಸಲ್ಲಿಸಬೇಕಾಗಿದೆ.
10. ನಿಗದಿತ ನಮೂನೆಯಲ್ಲಿ ದ್ವಿಪ್ರತಿಯಲ್ಲಿ ಒಪ್ಪಂದದ ಪತ್ರಗಳನ್ನು ಸಲ್ಲಿಸತಕ್ಕದ್ದು. (ಅದರಲ್ಲಿ ಒಂದಕ್ಕೆ ಸೂಕ್ತ ಸ್ಟಾಂಪ್ ಹಾಕಿರಬೇಕು)
11. ವಿತರಣಾ ಮಾರ್ಗದ ಕೇಬಲ್‌ನ ವಿಸ್ತರಣೆ ಆದ ನಂತರ ವಿದ್ಯುತ್ ಸರಬರಾಜಿಗೆ ವ್ಯವಸ್ಥೆ ಮಾಡಲಾಗುವುದು. ಮೇಲಿನ ಎಲ್ಲಾ ಅವಶ್ಯಕ ನಿಬಂಧನೆಗಳೂ ಈ ಪತ್ರದ ದಿನಾಂಕದಿಂದ ~~ಮೂರು~~ ತಿಂಗಳುಗಳ ಒಳಗಾಗಿ ಈಡೇರಿಸಬೇಕು. ಈ ನಿಟ್ಟಿನಲ್ಲಿ ವಿಫಲವಾದರೆ, ವಿದ್ಯುತ್ ಮಂಜೂರಾತಿಯು ತನ್ ತಾನೇ ರದ್ದಾಗುತ್ತದೆ ಮತ್ತು ಪಾವತಿ ಮಾಡಿರುವ ಠೇವಣಿಯನ್ನು ನಿಗಮಕ್ಕೆ ಮುಟ್ಟುಗೋಲು ಹಾಕಿಕೊಳ್ಳಲಾಗುತ್ತದೆ.

ತಮ್ಮ ವಿಶ್ವಾಸಿ

AE-ರ

ಸಹಾಯಕ ಕಾರ್ಯನಿರ್ವಾಹಕ ಇಂಜಿನಿಯರ್ (ನಿ.)

Name of work :- Drilling of borewell & providing pump & motor in ward No-5 Byatarayapura Sub-division

W. No. ಅನ್ನದಾನ ಲಾಡ್ಜಿನ 8ನೇ ಕ್ರಾಸಿನ ಹತ್ತಿರ ಬೋರ್‌ವೆಲ್

AE-05
ಸಹಾಯಕ ಅಭಿಯಂತರರು
ಬಿ.ಬಿ.ಎಂ.ಪಿ. ಬ್ಯಾಟರಾಯನಪುರ ಉಪ ವಿಭಾಗ

Assistant Executive Engineer
Byatarayanapura Division
B.B.M.P. Bangalore

W. No. 5. ಅಗ್ರಹಾರ ಅಂಚಿನ 8th ಕ್ರಾಸ್‌ನ ಪೈಪ್‌ಲೈನ್‌ನಲ್ಲಿ

ಸಹಾಯಕ ಅಭಿಯಂತರರು
ಬಿ.ಬಿ.ಎಂ.ಪಿ. ಬ್ಯಾಟರಾಯನಪುರ ಉಪ ವಿಭಾಗ

Assistant Executive Engineer
Byatarayanapura Sub Division
B.B.M.P. Bangalore
